



Initiating Projects

Module 2

1. How to get a project started
2. selecting project strategically
3. Project selection models (Numeric /Scoring Models and Non-numeric models)
4. Project portfolio process
5. Project sponsor and creating charter
6. Effective project team
7. Stages of team development & growth (forming, storming, norming & performing)
8. Team dynamics.



A photograph of a wooden staircase leading up a hill, with a quote overlaid. The staircase is made of dark wood and has a simple railing. The background is a misty, hilly landscape. The quote is written in a yellow, hand-drawn style.

Well begun is half done.

— Aristotle


Quotes.Casa



Why is starting a project important?

- Sets the foundation for success.
- Aligns team efforts with goals and resources.

Key Steps to Get Started:

- Define project goals and objectives.
 - Identify stakeholders and team members.
 - Develop a clear project plan and timeline.
- 

Steps to Get a Project Started

1. Identify the Problem or Opportunity:

1. Understand the need for the project.
2. Clearly define the problem to solve or the opportunity to seize.

2. Set Clear Objectives:

1. SMART objectives (Specific, Measurable, Achievable, Relevant, Time-bound).

3. Engage Stakeholders:

1. Identify key stakeholders and involve them early.

4. Develop a Business Case:

1. Outline the project's value and expected benefits.

5. Create a Project Charter:

1. Document that outlines scope, objectives, stakeholders, and deliverables.



&



Selection of Project

- ✓ Project initiation begins with the judicious selection of the organization's projects to align them with the organization's overall strategy.
- ✓ Evaluate and select projects that contribute to the organization's strategy



Strategic project selection



constraints of an organisation

- Limited resources
- Limited time
- Limited Finance
- Limited human resource
- Limited material
- Limited scale

select the project with maximum benefits to the organization

Importance of Selecting Projects Strategically

Why Strategic Selection Matters:

- Maximizes return on investment (ROI).
- Aligns projects with organizational goals.
- Optimizes resource allocation.



Key Criteria for Strategic Project Selection

1. Alignment with Organizational Goals:

1. How does the project fit with long-term objectives?

2. Financial Viability:

1. Evaluate cost, benefits, and ROI.

3. Feasibility:


1. Assess technical, resource, and time feasibility.

4. Risk Assessment:

1. Identify and evaluate potential risks.

5. Stakeholder Support:

1. Ensure stakeholder buy-in and support.





Methods for Strategic Project Selection

1. Numeric/Scoring Models:

1. Assign scores to projects based on specific criteria.
2. Example: Benefit-Cost Ratio (BCR), ROI.


2. Non-Numeric Models:


1. Use qualitative assessments.
 2. Example: Strategic alignment or expert judgment.
- 



Describing a project

- elements {
- ☐ People
 - ☐ Processes
 - ☐ Products






People


Team

Describing the team


- Skills required
- Experience
- Availability
- Budget to get them on board


Stakeholders

- Identifying and defining the roles
 - Initiating communication
 - Meeting with stakeholders
- 




Process


- Methodology
 - Tools
 - Managing risk
- 



Product

- Requirement analysis
 - Identify scope and deliverables
 - Setting deliverables
 - Budget and timings
 - Setting measures of success
- 

The process of initiating a project

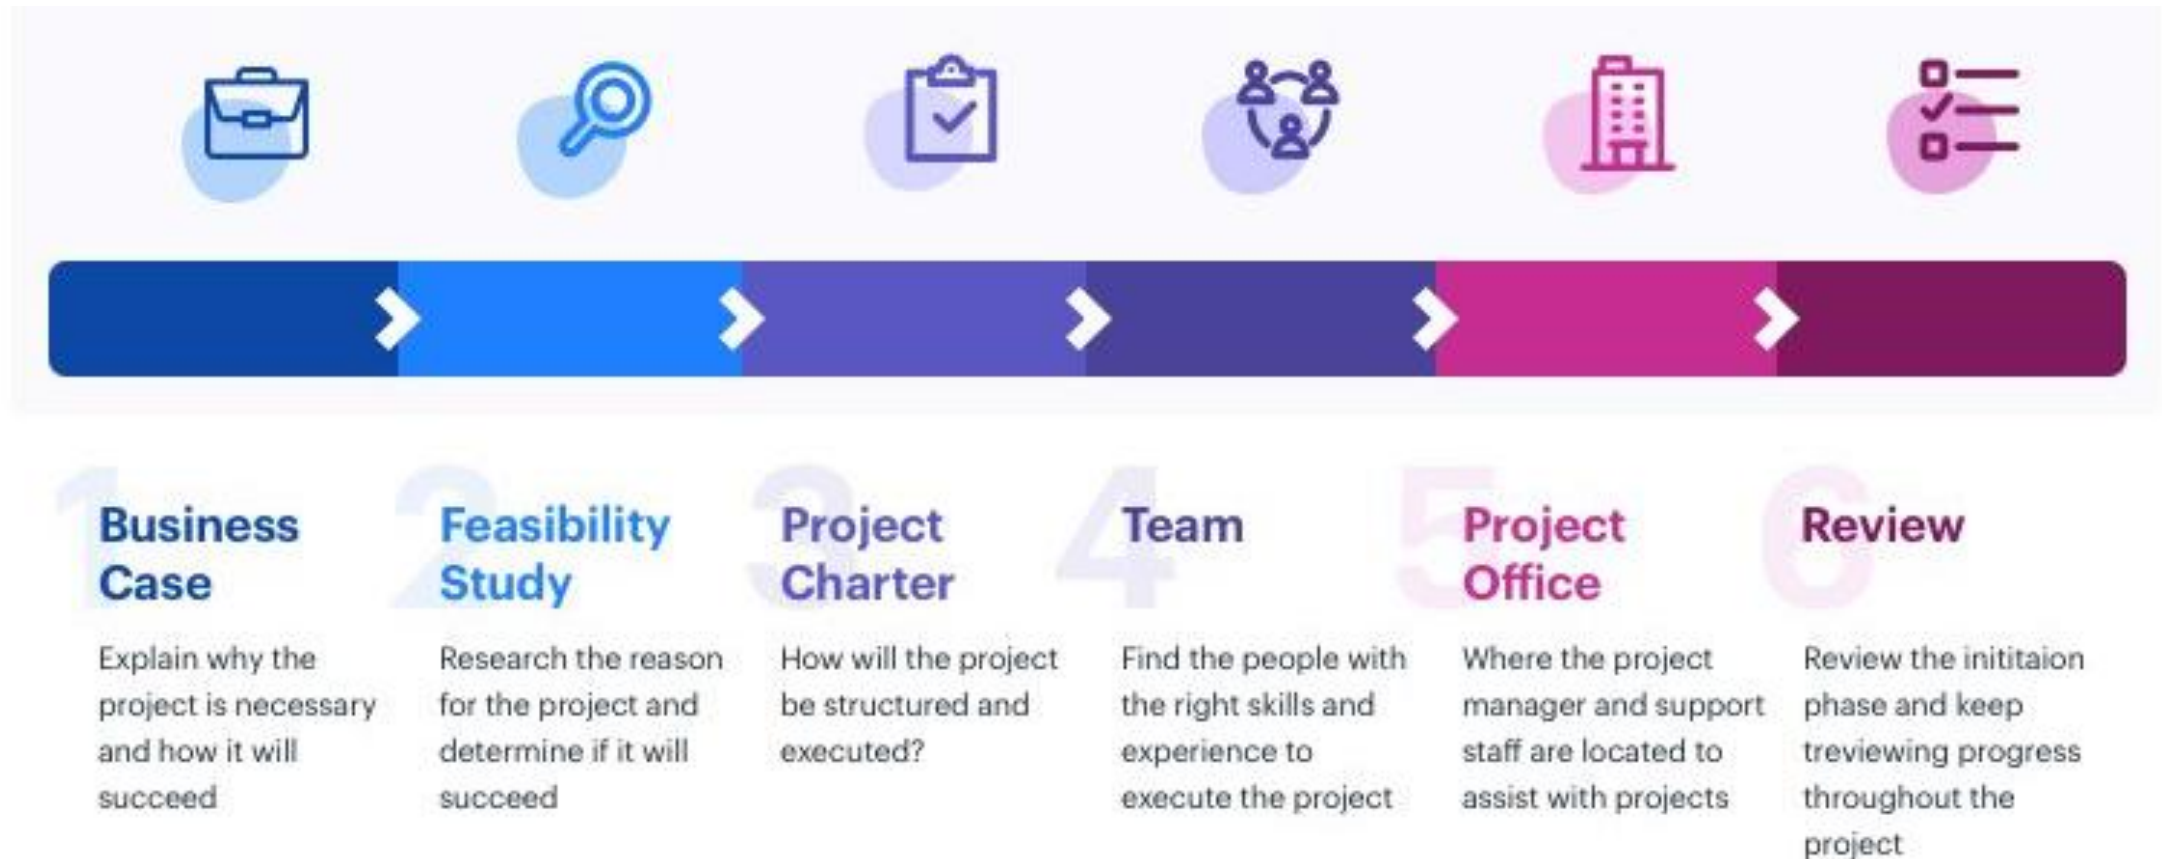

Project selection models

1. Non-numeric models
2. Numeric models

Non-numeric project selection models

1. sacred cow
2. operating necessity
3. competitive necessity
4. product line extension
5. comparative benefit model
6. Q-sort model

Sacred cow

- Senior members of the organization suggest a project out of their own understanding and expertise
- Initiated out of an apparent opportunity of taking a chance of an un-established idea for a new product
- Project is created immediately
- Whatever the boss proposes becomes the project
- Project continuous till it finishes or until the senior declared it as a failure



The Operating Necessity

If a flood is threatening the plant, a project to build a protective dyke does not require much formal evaluation, which is an example of this scenario. If the project is required in order to keep the system operating, the primary question becomes: Is the system worth saving at the estimated cost of the project?




Competitive Necessity

- An organization always like to stay ahead in the competition




Product line extension

- Initiated for the development and distribution of new products

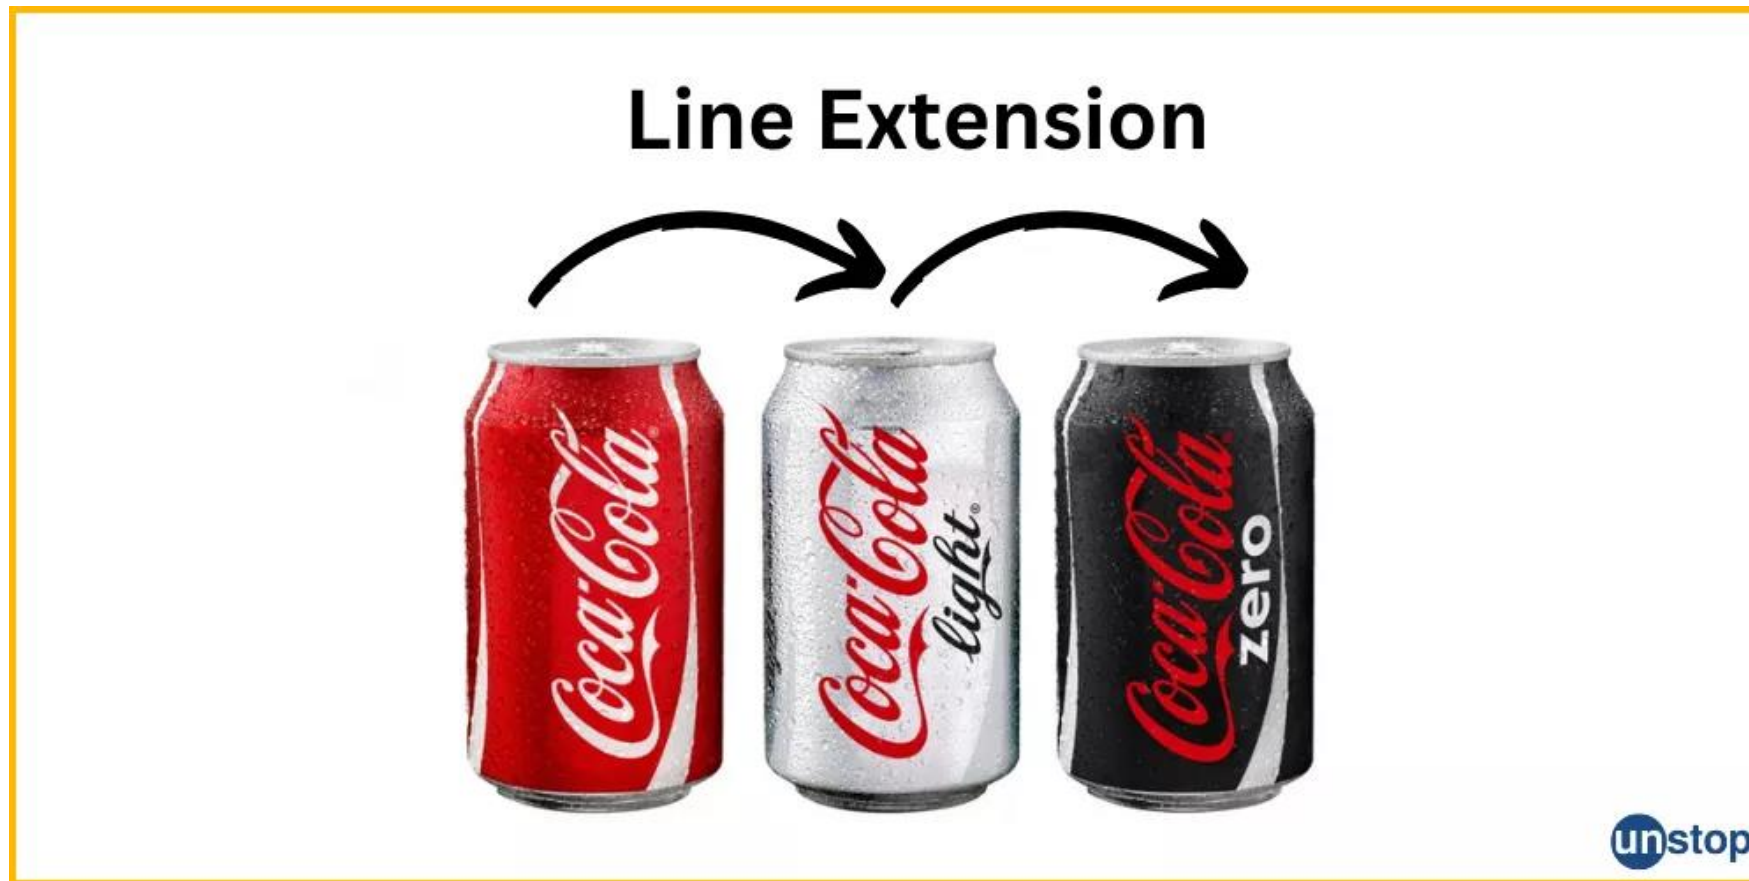

Comparative benefit

- Used when there are several projects up for consideration
- selection is made on the basis of comparative study and a project is selected which provides maximum benefit to the company
- Selection is based on the perception of the selection committee members

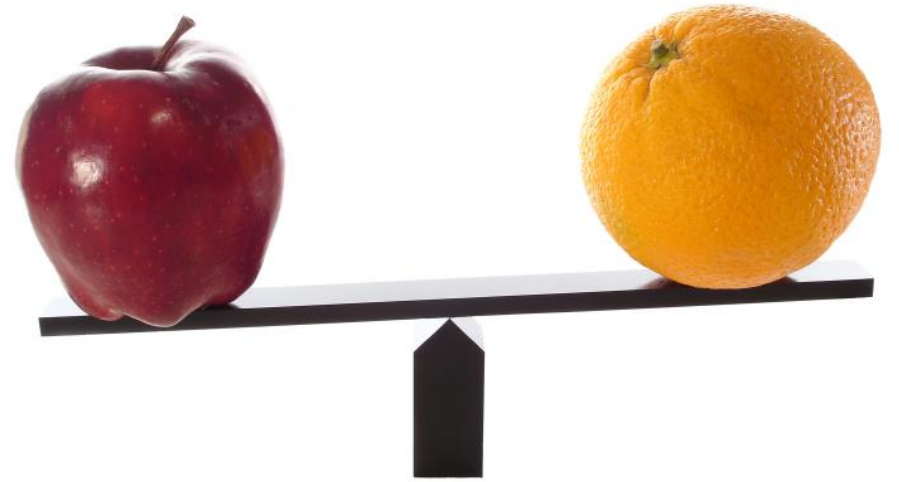

Numeric project selection models

Profit/Profitability Models

1. Payback period
2. accounting rate of return
3. break even analysis
4. cost benefit analysis
5. net present value (NPV)
6. internal rate of return (IRR)

Scoring Models

1. Unweighted 0-1 Factor Model
2. Unweighted Factor Scoring Model
3. weighted Factor Scoring Model

Payback period

- Calculate the time period that will be required for the project to generate enough return to recover the initial investment
- it focuses on measuring the cash inflows without looking at the time value of the money



Payback Period
Formula

$$= \frac{\text{Initial Investment Made}}{\text{Net Annual Cash Inflow}}$$


Two new Internet site projects are proposed to a young start-up company. Project A will cost \$250,000 to implement and is expected to have annual net cash flows of \$75,000. Project B will cost \$150,000 to implement and should generate annual net cash flows of \$52,000. The company is very concerned about their cash flow. Using the payback period, which project is better, from a cash flow standpoint?

Accounting rate of return (ARR)

- It is expressed as a percentage of the earnings of the investment
- ignore time value of the money




$$\text{Accounting Rate of Return Formula} = \frac{\text{Average Annual Profit}}{\text{Initial Investment}}$$



Break even analysis

- Determines at what stage of the project it will become profitable
- in defines a situation where your income and expenses match and thus you are neither making money nor losing

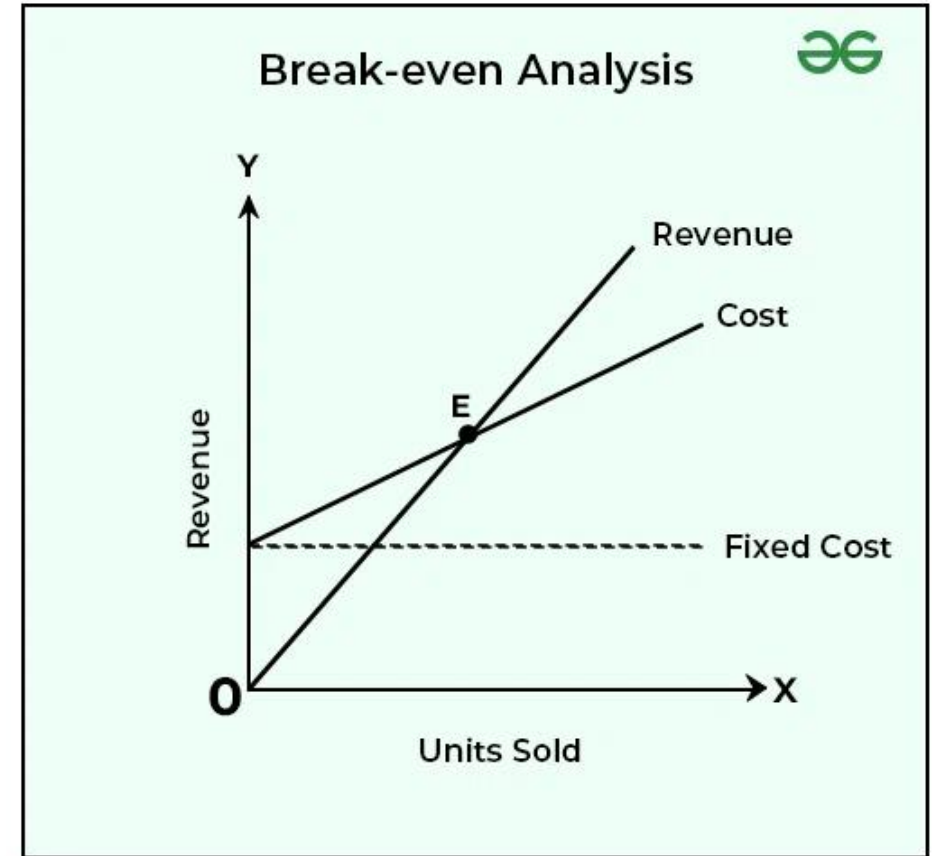

Net present value

- Also referred as Discounted Cash Flow model
- determines the net present value of all cash flows by discounting them by the required rate of return

$$\text{NPV (project)} = A_0 + \sum_{t=1}^n \frac{F_t}{(1+k)^t}$$

where

F_t = the net cash flow in period t ,

k = the required rate of return, and

A_0 = initial cash investment (because this is an outflow, it will be negative).

To include the impact of inflation (or deflation) where p_t is the predicted rate of inflation during period t , we have

$$\text{NPV (project)} = A_0 + \sum_{t=1}^n \frac{F_t}{(1+k+p_t)^t}$$

\$100,000 investment with a net cash inflow of \$25,000 per year for a period of eight years, a required rate of return of 15 percent, and an inflation rate of 3 percent per year, we have

$$\text{NPV (project)} = A_0 + \sum_{t=1}^n \frac{F_t}{(1+k)^t}$$

$$\begin{aligned}\text{NPV (project)} &= -\$100,000 + \sum_{t=1}^8 \frac{\$25,000}{(1 + 0.15 + 0.03)^t} \\ &= \$1939\end{aligned}$$

A four-year financial project has net cash flows of \$20,000; \$25,000; \$30,000; and \$50,000 in the next four years. It will cost \$75,000 to implement the project. If the required rate of return is 0.2, conduct a discounted cash flow calculation to determine the NPV.

$$\text{NPV (project)} = A_0 + \sum_{t=1}^n \frac{F_t}{(1 + k + p_t)^t}$$

Internal Rate of Return If we have a set of expected cash inflows and cash outflows, the internal rate of return is the discount rate that equates the present values of the two sets of flows. If A_t is an expected cash outflow in the period t and R_t is the expected inflow for the period t , the internal rate of return is the value of k that satisfies the following equation (note that the A_0 will be positive in this formulation of the problem):

$$A_0 + A_1/(1 + k) + A_2/(1 + k)^2 + \cdots + A_n/(1 + k)^n = R_1/(1 + k) + R_2/(1 + k)^2 + \cdots + R_n/(1 + k)^n$$

The value of k is found by trial and error.

Scoring

Unweighted 0–1 Factor Model

Project _____		
Rater _____	Date _____	
	Qualifies	Does Not Qualify
No increase in energy requirements	X	
Potential market size, dollars	X	
Potential market share, percent	X	
No new facility required	X	
No new technical expertise required		X
No decrease in quality of final product	X	
Ability to manage project with current personnel		X
No requirement for reorganization	X	
Impact on work force safety	X	
Impact on environmental standards	X	
Profitability		
Rate of return more than 15% after tax	X	
Estimated annual profits more than \$250,000	X	
Time to break-even less than 3 years	X	
Need for external consultants		X
Consistency with current line of business		X
Impact on company image		
With customers	X	
With our industry		X
Totals	12	5

Unweighted Factor Scoring Model

Weighted Factor Scoring Model When numeric weights reflecting the relative importance of each individual factor are added, we have a weighted factor scoring model. In general, it takes the form

$$S_i = \sum_{j=1}^n s_{ij} w_j$$

where

S_i = the total score of the i th project,

s_{ij} = the score of the i th project on the j th criterion, and

w_j = the weight of the j th criterion.


20. A company has established a project team to identify a location for a new manufacturing facility. Use a weighted scoring model to analyze three candidate locations (A, B, C) for setting up the new factory. The relative weights for each criterion are shown in the following table. A score of 1 represents unfavorable, 2 satisfactory, and 3 favorable.

		Location		
Category	Weight	A	B	C
Labor costs	20	1	2	3
Labor productivity	20	2	3	1
Labor supply	10	2	1	3
Union relations	10	3	3	2
Material supply	10	2	1	1
Transport costs	25	1	2	3
Infrastructure	5	2	2	2

21. (a) Compare your answer in Problem 20 to the answer you would have found if you had used an unweighted, 0-1 scoring model. Assume that a score of 1 means does not qualify and a 2 or 3 means it does qualify.

As shown below, that would result in a score of five for all three projects.

Category	Location		
	A	B	C
Labor costs		x	x
Labor productivity	x	x	
Labor supply	x		x
Union relations	x	x	x
Material supply	x		
Transport costs		x	x
Infrastructure	x	x	x
Count	5	5	5




Activity: Numeric models of Project Selection

Tesla, a global leader in electric vehicles (EVs), is considering setting up a **manufacturing plant in India** to tap into the rapidly growing EV market. The company has three potential investment options:

1. **Greenfield EV Factory in Gujarat** (Build a new facility from scratch)
2. **Joint Venture with Tata Motors** (Partner with an existing Indian automaker)
3. **Import-Based Sales Model** (Import and sell Tesla vehicles directly)

Your task is to evaluate these options using **numeric project selection models** and recommend the best strategy.

1. Which project is financially viable based on the numeric models?
 2. What are the risks and challenges of each approach?
 3. If you were Tesla's CEO, which option would you choose and why?
- 

Project Data: Investment Details

Project A:

Greenfield EV Factory

- Initial Investment: ₹10,000 Crores
- Annual Revenue Projection: ₹3,000 Crores
- Annual Operating Cost: ₹1,500 Crores
- Expected Lifetime: 10 years
- Discount Rate: 12%

Project B:

Joint Venture with Tata Motors

- Initial Investment: ₹5,000 Crores
- Annual Revenue Projection: ₹2,200 Crores
- Annual Operating Cost: ₹1,200 Crores
- Expected Lifetime: 8 years
- Discount Rate: 10%

Project C:

Import-Based Sales Model


- Initial Investment: ₹3,000 Crores
- Annual Revenue Projection: ₹1,500 Crores
- Annual Operating Cost: ₹900 Crores
- Expected Lifetime: 6 years
- Discount Rate: 9%



Project Portfolio Process

Project Portfolio

- A Project Portfolio is a collection of projects managed and coordinated together to achieve strategic business objectives.
- It helps organizations allocate resources efficiently, prioritize high-impact projects, and align work with long-term goals.

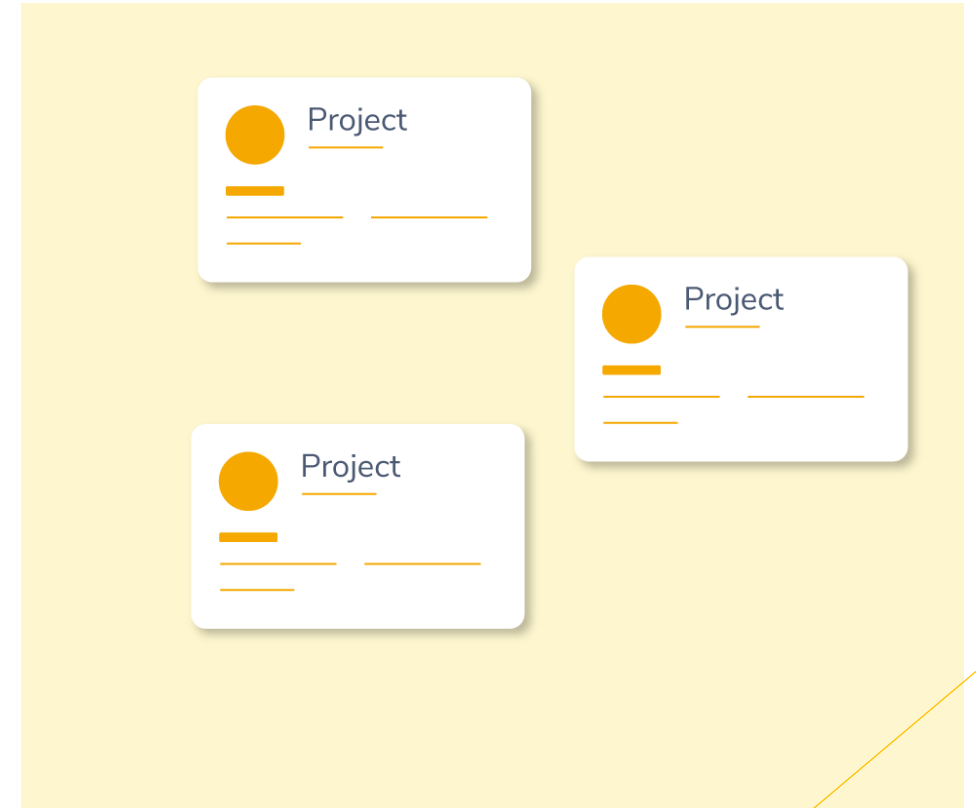

Project Portfolio Process


- A structured approach to selecting and managing multiple projects.
- Ensures alignment with business goals and optimal resource utilization.
- It involves identifying, prioritizing, and monitoring projects.
- Occurs throughout lifecycle of project



Project Portfolio Process

Functions of PPP

- To prioritize the list of available projects
- To intentionally limit the number of overall projects being managed so the important projects get the resources and attention they need
- To identify projects that best fit the organization's goals and strategy
- To eliminate projects that incur excessive risk and/or cost
- To eliminate projects that bypassed a formal selection process and may not provide benefits corresponding to their risks and/or costs
- To keep from overloading the organization's resource availability
- To balance short-, medium-, and long-term returns



Project Portfolio Process

Step 1: Establish a Project Council

Step 2: Identify Project Categories & Criteria

Step 3: Collect Project Data


Step 4: Assess Resource Availability

Step 5: Reduce Project and Criteria Set

Step 6: Prioritize Projects within Categories

Step 7: Select the projects to be funded and held in reserve

Step 8: Implement the Process



Step 1: Establish a Project Council

- Form a governing body responsible for portfolio decisions.
- Includes senior executives, project managers, and key stakeholders.
- Ensures alignment with organizational goals.
- Also responsible for allocating funds, resources and skills



Step 2: Identify Project Categories & Criteria


- Various projects categories are identified
 - So that it will be spread appropriately to meet various goals of the organisation
 - Discriminate between good and better projects
 - Criteria's are weighted to reflect their relative importance
- First step is to list goals of each existing and proposed project

Step 2: Identify Project Categories & Criteria

Aggregate Project Plan

Categories proposed by Weelwright and Clark

- **Breakthrough Projects** – High-risk, high-reward (e.g., New AI-powered technology).
- **Platform Projects** – Builds on existing technologies (e.g., Upgrading a cloud system).
- **Derivative Projects** – Small improvements (e.g., Minor software updates)
- **R&D Projects** – Long-term research for innovation (e.g., Self-driving cars).

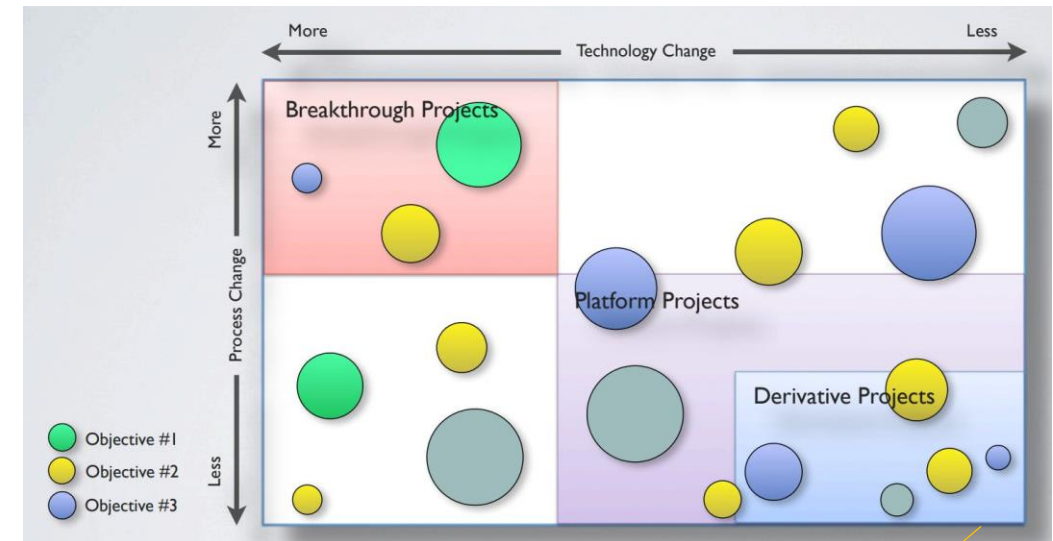

Step 2: Identify Project Categories & Criteria

Aggregate Project Plan

1. A strategic framework for managing multiple projects.
2. Ensures alignment with company goals and resource availability.
3. Helps in balancing short-term and long-term projects.
4. Ensures a balanced mix of project types.
5. Helps in effective resource allocation (budget, manpower, technology).
6. Improves decision-making on which projects to prioritize.

Step 3: Collect Project Data

- Gather detailed information on all proposed projects.
- Identify the estimated budget, resource needs, timeline, and risks.
- Evaluate the project's alignment with strategic goals.
- **Example:** A company considering an AI-driven customer support chatbot will collect data on cost, potential benefits, required tech stack, and risk factors.



Step 4: Assess Resource Availability

- Analyze the **availability of financial, human, and technical resources.**
- Ensure that projects do not exceed capacity limits.
- Prioritize projects based on **resource feasibility.**
- **Example:** If a company has **limited AI developers**, it may **delay or outsource** a Chatbot project.



Step 5: Reduce Project and Criteria Set

- Filter out **projects** that are **redundant**, **low-priority**, or **misaligned** with strategy.
- Reduce the **selection criteria** to focus on **key decision factors** like ROI, innovation, or customer impact.
- Example: A company might eliminate a **redundant cybersecurity project** if another security upgrade is already in place.



Step 6: Prioritize the Projects within Categories

- Apply score and criterion weights to rank projects
- Rank projects based on their value, feasibility, and alignment with company goals.
- Assign weightage to different evaluation criteria (e.g., ROI = 40%, Market Impact = 30%, Risk = 30%).
- Council summaries return from the project
- Example: A high-impact, medium-risk AI Chabot may get prioritized over a high-risk, uncertain AR project.

	Revenue potential	Customer value	Strategic value	Risk potential		
Weighting	10	10	5	5	Total score	Rank
Project 1	5	4	5	4	135	1
Project 2	2	3	2	2	70	4
Project 3	3	5	4	3	115	2
Project 4	1	5	2	4	90	3

Step 7: Select the Projects to be funded and held reserve


- Determine the **mix of projects** across various categories
- **Rank** the projects in categories
- Leave **20-25 %** of the organisations **resources for new opportunities**, crises in existing project, errors in estimate etc
- **Commit fewer projects but allocate sufficient fund** for project selection
- Keep some projects on **hold** as backups in case resources free up or priorities change.
- Example: A **critical cybersecurity upgrade** and **AI Chabot** are selected, while **an IoT project** is kept in reserve.

Step 8: Implement the Process

- Finalize the **selected projects** and allocate budgets.
- Assign project teams and set **clear timelines**.
- Document the reasons for project cancellation, non selection etc.
- Example: The selected AI Chabot and cybersecurity projects begin development, and regular reviews ensure alignment with goals.



‘Process must be repeated on a regular basis’




Activity: Project Portfolio Process

You are part of the **Strategic Project Selection Committee** of XYZ Corp., responsible for choosing projects that align with the company's vision:

"To be a leader in sustainable and innovative technology solutions by 2030."

Your company has a **budget of ₹50 crore** and a **team of 100 employees** for the next financial year. You must choose projects that align with the vision while considering constraints like costs, manpower, and expected benefits.



Activity: Project Portfolio Process

Ongoing Projects

Project Name	Investment (₹ Crore)	Manpower Required	Completion Time Remaining	Expected Return	Strategic Fit
Smart Grid Technology	12	20	2 years	₹45 crore	High
AI-Powered Customer Support	7	15	1 year	₹30 crore	Medium
Electric Vehicle Battery Innovation	15	35	3 years	₹60 crore	High

New Projects

Project Name	Investment (₹ Crore)	Manpower Required	Completion Time	Expected Return	Strategic Fit (Low/Medium/High)
Green Tech R&D	20	30	3 years	₹70 crore	High
AI-Based Automation	15	25	2 years	₹50 crore	Medium
Solar EV Prototype	18	40	4 years	₹80 crore	High
Smart Healthcare IT	10	20	3 years	₹40 crore	High
Digital Marketing Expansion	8	15	1 year	₹25 crore	Medium

Activity: Project Portfolio Process

Step 1: Establish a Project Council

Step 2: Identify Project Categories & Criteria

Step 3: Collect Project Data

Step 4: Assess Resource Availability

Step 5: Reduce Project and Criteria Set

Step 6: Prioritize Projects within Categories

Step 7: Select the projects to be funded and held in reserve


Step 8: Implement the Process

Module 2

1. How to get a project started
2. selecting project strategically
3. Project selection models (Numeric /Scoring Models and Non-numeric models)
4. Project portfolio process
5. Project sponsor and creating charter
6. Effective project team
7. Stages of team development & growth (forming, storming, norming & performing)
8. Team dynamics.

Project sponsor

- A Project Sponsor is a senior executive or stakeholder who champions, funds, and supports a project from initiation to completion.
- They ensure the project aligns with the organization's goals and provide the necessary resources and decision-making authority to keep it on track.

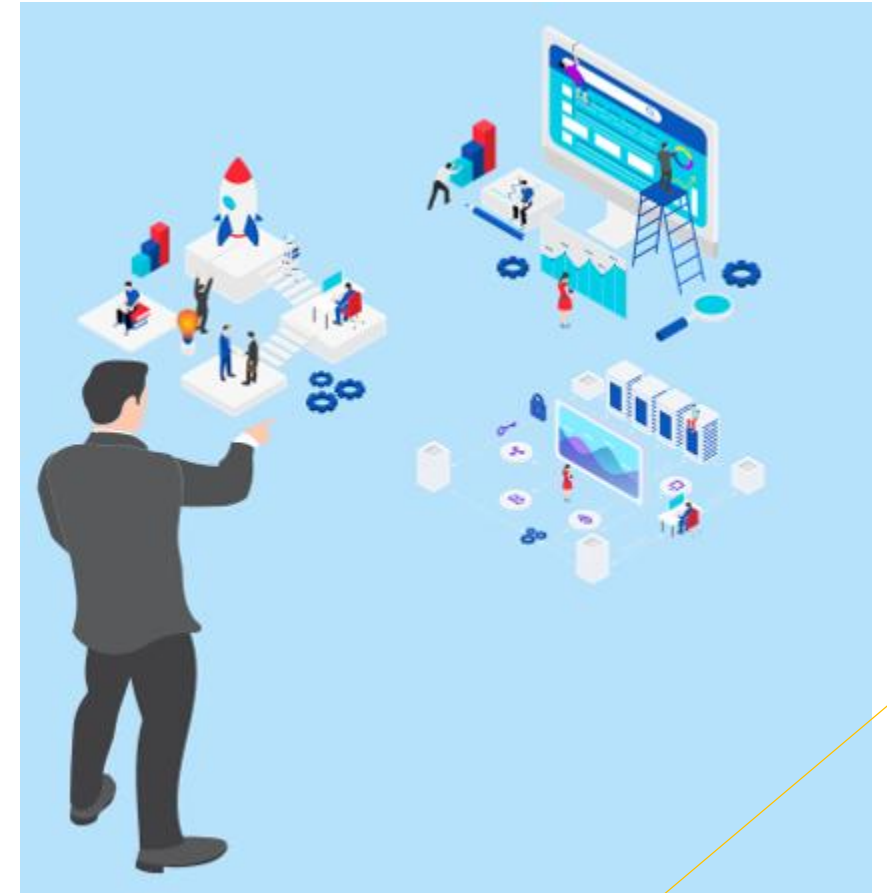

Project sponsor

- They are the **reason for the project**.
- While **they don't manage the day-to-day operations** of a project, they are **above the project manager** in terms of project hierarchy.
- Most likely, the project sponsor has been involved with the project from the very beginning. They were the one who helped conceive it and advocated for it.
- The project sponsor can vary according to the project. For example, a government project is going to have a state official as project sponsor who will work with the construction company's project manager. However, in an IT project, the project sponsor might be the chief information officer.

Project sponsor

Project 1: Building a New Library in a College

Project Sponsor: The College Principal

Project 2: Developing a New Mobile Banking App


Project Sponsor: The Chief Financial Officer (CFO) of the bank.



Project sponsor

Key Responsibilities of a Project Sponsor

- **Approves Project Charter** – Defines goals and scope.
- **Secures Funding** – Ensures budget allocation.
- **Aligns with Organizational Goals** – Ensures project supports business strategy.
- **Supports the Project Manager** – Provides guidance and removes obstacles.
- **Engages Stakeholders** – Communicates with leadership and teams.

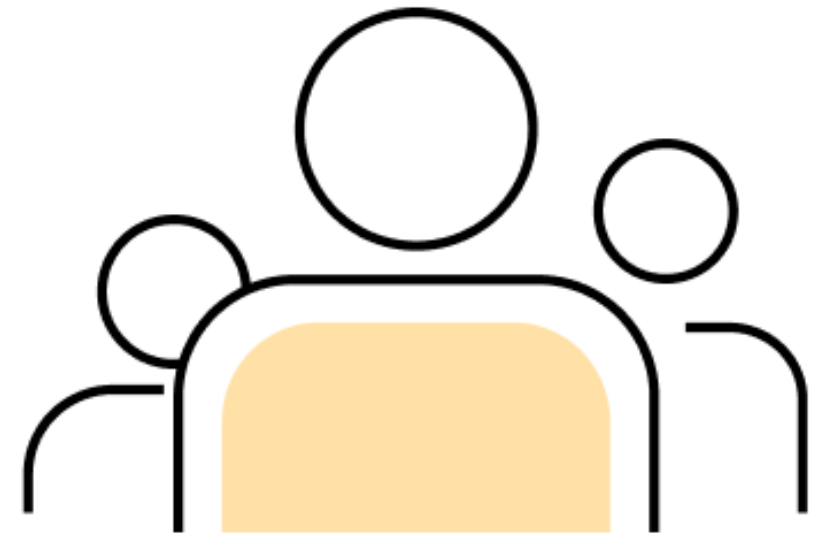

Project sponsor

Project Sponsor vs. Project Manager

Aspect	Project Sponsor	Project Manager
Strategic Focus	Aligns project with goals	Executes project plan
Decision-Making	High-level decisions	Day-to-day operations
Resource Authority	Controls budget/resources	Manages team and tasks

Project sponsor

Hierarchy in Project




Project Charter

What is a Project Charter?


- A document that formally authorizes a project, outlining objectives, scope, key stakeholders, and responsibilities.
- It's created early in a project's lifecycle to get approval from stakeholders.
- The charter serves as a reference and guide for the project team and stakeholders.

PROJECT CHARTER					
Project Title	Write Project Name here		Project Manager	Project Manager	
Project Start Date	Start date?	Project End Date	End date?	Project Sponsor	Project Sponsor
Business Need					
Write business need here.					
Project Scope		Deliverables			
Write project scope here.		List project deliverables here.			
Risks and Issues		Assumptions/Dependencies			
List the project risks & issues here!		List project assumptions/dependencies here.			
www.excelonist.com					
Milestones Schedule					
Milestone		Target Completion Date	Actual Date		
Write milestone 1 here		Target date?	Actual Date?		
Write milestone 2 here		Target date?	Actual date		
Project Team		Approval/Review Committee			
Project Manager	Project Manager?	Sponsor	Project Sponsor?		
Technical Lead	Project Technical Lead?	Business Division Head	Division Head?		
Team Members	List project team members here!	Business Unit Head	Unit Head?		
		Finance Manager	Finance Manager?		



Project Charter

Key Components of a Project Charter

- **Project Title & Description** – Name and brief summary of the project.
 - **Project Objectives** – Clear, measurable goals.
 - **Scope Statement** – Defines what is included/excluded in the project.
 - **Key Stakeholders** – Identifies project sponsor, manager, and team.
 - **Budget & Resources** – Estimated cost and resource allocation.
 - **Timeline & Milestones** – Key dates and phases of the project.
 - **Risks & Assumptions** – Identifies potential risks and project constraints.
- 

Project Charter

Who Creates the Project Charter?

- The **Project Manager** is typically responsible for drafting the Project Charter.
- They collaborate with the **Project Sponsor**, key stakeholders, and relevant teams to define project objectives, scope, budget, and risks.

Who Approves the Project Charter?

- The **Project Sponsor** (a senior executive or funding authority) reviews and approves the charter.
- In some organizations, **senior management** or a **Project Steering Committee** may also be involved in approval.

PROJECT CHARTER

Project Title	Project and Portfolio Management Tool			Project Manager	Sameer Patel
Project Start Date	May 21, 2017	Project End Date	August 31, 2017	Project Sponsor	Randy Hadden
Business Need					
All Information Technology projects that require agreement on the Memorandum of Understanding between the Customer and the Service Provider are approved through email. This project was initiated to reduce the manual approvals and create a system to obtain and track the approvals to reduce any discrepancies and loss of data.					
Project Scope			Deliverables		
Create an in-house PPM to include all Global IT projects.			1. Generate consolidated project status report 2. Extract Global Headcount details for all projects		
Risks and Issues			Assumptions/Dependencies		
1. Data discrepancy due to large amount of projects 2. Involvement of multiple teams			1. All Global IT projects to be added to the tool 2. Managers to provide regular updates for the projects		
Financials					
Budget to complete this project is \$3000					
Milestones Schedule					
Milestone			Target Completion Date		Actual Date
Upload all Global IT Projects to the tool			May 20, 2017		
Complete UAT testing for the tool			July 30,2017		
Project Team			Approval/Review Committee		
Project Manager	Randy Hadden		Sponsor	Randy Hadden	
Project Manager	Sameer Patel		Business Division Head	Aniket Bhonsle	
Team Members	Vice President, Senior Manager, Analyst		Business Unit Head	Sunil Rajan	
			Finance Manager	Ketan Shah	

Activity - Creating a Project Charter for a College Fest

1. **Project Title:** Name of the Fest.
2. **Project Objectives:** Goals and impact.
3. **Project Scope:** Inclusions & exclusions.
4. **Stakeholders:** Faculty advisors, students, sponsors, participants.
5. **Budget Estimate:** Venue, decorations, logistics, promotions.
6. **Resources Required:** Manpower, permits, sponsorship.
7. **Major Risks:** Crowd control, funding, event coordination.
8. **Project Sponsor:** Who funds and approves (College Admin, External Sponsors).

Effective Project Teams

- Good and effective team building is an ability to turn the group of individuals into the strong and organized system walking towards the common goal
- Project managers require the skills to identify, build, maintain, motivate, lead, and inspire project teams to achieve high team performance and to meet the project's objectives.



Effective Project Teams


Characteristics of an Effective Project Team

- **Clear Goals** – Everyone understands the project objectives.
- **Defined Roles & Responsibilities** – Each member knows their tasks.
- **Strong Leadership** – A project manager guides the team.
- **Open Communication** – Transparency and feedback are encouraged.
- **Collaboration & Trust** – Teamwork ensures smooth execution.
- **Adaptability** – Ability to handle changes and challenges.



Stages of Team Development

- The process of learning to work together effectively is known as team development.
- Teams evolve over time through structured phases.
- Understanding these stages helps manage teamwork effectively.
- Bruce Tuckman proposed the Forming-Storming-Norming-Performing-Adjourning model.

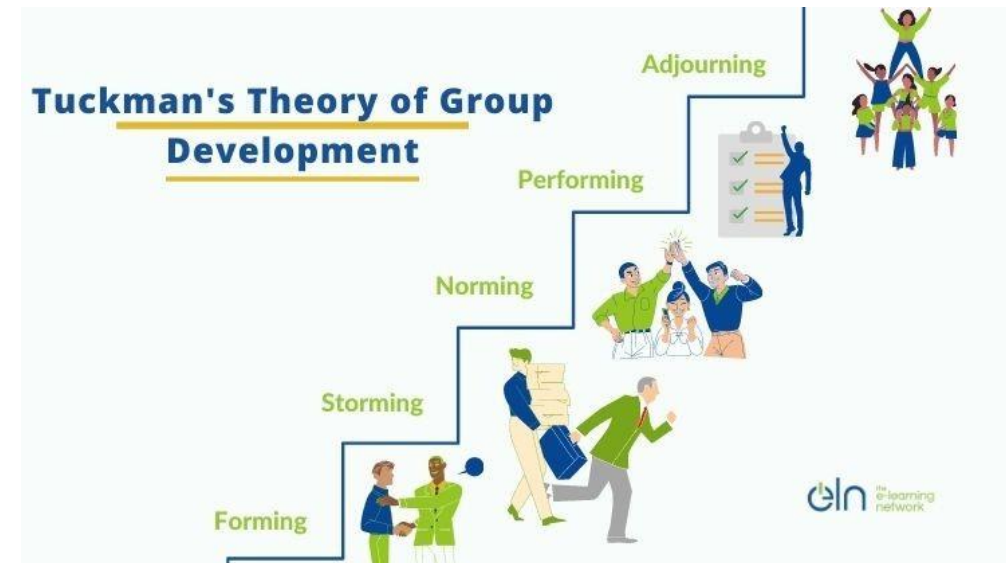

Stages of Team Development

Stage 1 - Forming (Getting Started)

- Team members are introduced.
- Roles and responsibilities are unclear.
- High dependency on the leader for guidance.
- Excitement and uncertainty coexist.

Tip: Encourage open discussions to build trust.



Example: A group of students forming a team for a college fest, unsure of their tasks but excited about the event.

Stages of Team Development

Stage 2 - Storming (Conflict & Challenges)

- Differences in opinions and work styles arise.
- Frustrations and conflicts occur.
- Power struggles may emerge.
- Some members may feel excluded.

Tip: Address conflicts early through open communication.

Example: Team members argue over event themes and budget allocations.



Stages of Team Development

Stage 3 - Norming

(Collaboration & Understanding)

- Team members accept each other's strengths.
- Roles and responsibilities become clearer.
- Improved cooperation and productivity.
- Team spirit develops.

Tip: Encourage team bonding and constructive feedback.

Example: The event team finalizes tasks, resolves conflicts, and starts working efficiently.



3. NORMING

Stages of Team Development

Performing (High Productivity)

- The team functions smoothly and efficiently.
- Roles are well-defined, and members are self-motivated.
- Trust and collaboration are at their peak.
- Problems are solved with minimal friction.

Tip: Keep motivating the team and recognize efforts.

Example: The fests team executes promotions, ticket sales, and guest arrangements seamlessly.



Stages of Team Development

Stage 5 - Adjourning (Project Completion)

- Project comes to an end, and the team disbands.
- Mixed emotions: pride, relief, or sadness.
- Team members reflect on successes and lessons learned.

Tip: Celebrate achievements and document key takeaways.

Example: The college fest is successfully conducted, and the team shares feedback before moving on.




Stages of Team Development

Activity - Identify the Team Stage

Identify which stage of team development they represent.

- A newly formed robotics team meets for the first time.
- Members argue over who will lead the project.
- The team efficiently executes a marketing campaign.
- The project ends, and the team members part ways.

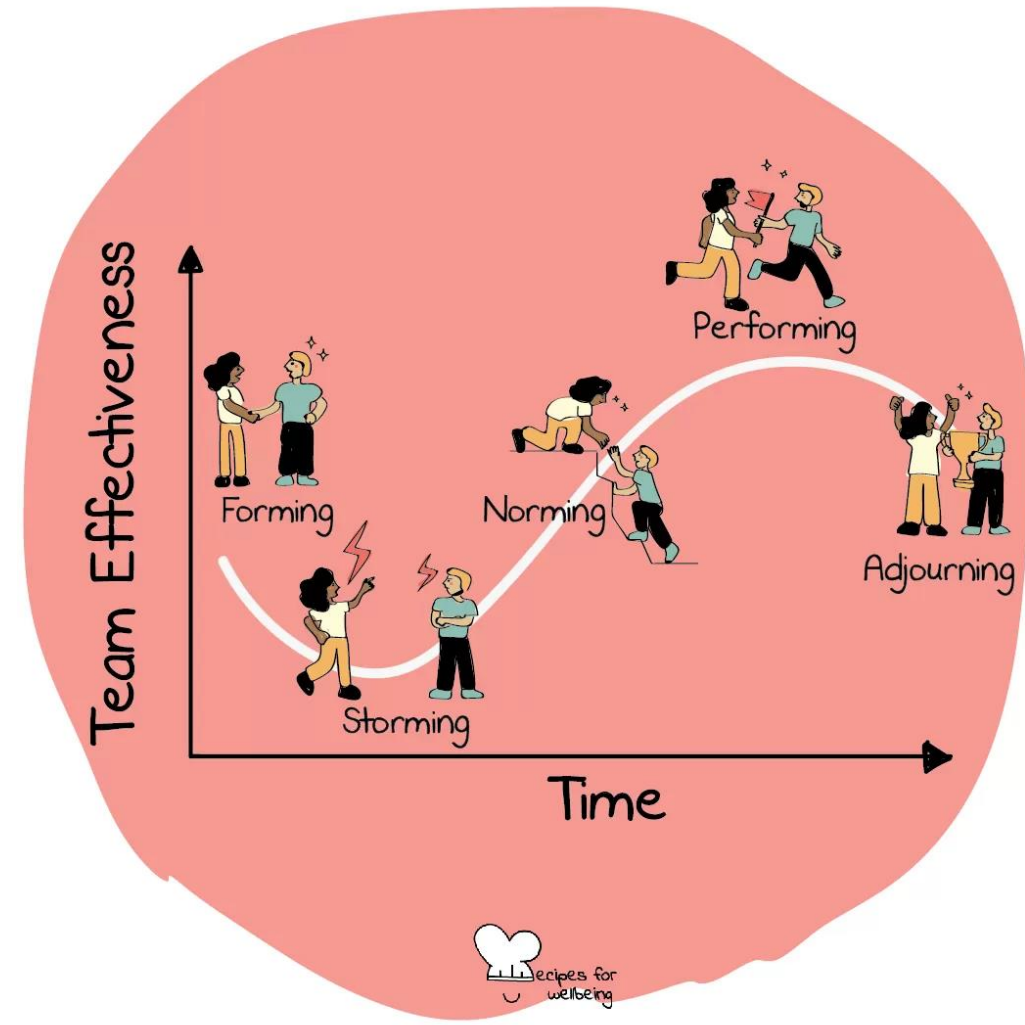

Team Dynamics

- Team dynamics are those psychological forces influencing the direction of your team's performance and behavior.
- Those dynamics are created by the personalities involved and how they interact.
- Influence how a team performs and collaborates.
- Affected by communication, leadership, trust, and roles.



Team Dynamics

Why are Team Dynamics Important?

- Enhance productivity and efficiency.
- Foster innovation and creative problem-solving.
- Prevent conflicts and improve work relationships.



Team Dynamics

Key Factors Affecting Team Dynamics

- **Roles & Responsibilities** – Clear role distribution avoids confusion.
- **Communication** – Open and transparent discussions prevent misunderstandings.
- **Trust & Respect** – Builds a strong foundation for collaboration.
- **Leadership Style** – Influences decision-making and motivation.
- **Conflict Resolution** – Healthy debates vs. disruptive conflicts.
- **Diversity & Inclusion** – Different perspectives enrich problem-solving.



Team Dynamics

Types of Team Dynamics

Positive Team Dynamics

- ✓ Team members support each other.
- ✓ Effective collaboration and goal alignment.
- ✓ High morale and motivation.

Negative Team Dynamics

- ✗ Frequent conflicts and misunderstandings.
- ✗ Lack of participation and commitment.
- ✗ Poor communication leads to inefficiency.



Team Dynamics

Examples of Team Dynamics in Action

Example of Positive Dynamics

🏆 A college fest organizing team works smoothly, respects each other's inputs, and meets deadlines.

Example of Negative Dynamics

❌ A group project where members argue over responsibilities, leading to delays and poor performance.



Team Dynamics

Improving Team Dynamics

- ✓ **Set Clear Goals** – Define objectives and expectations early.
- ✓ **Encourage Open Communication** – Create a safe space for sharing ideas.
- ✓ **Define Roles & Responsibilities** – Avoid confusion and overlap.
- ✓ **Build Trust** – Promote transparency and honesty.
- ✓ **Foster Inclusivity** – Value diverse opinions and perspectives.
- ✓ **Resolve Conflicts Proactively** – Address issues before they escalate.

Team Dynamics

Activity - Analyzing Team Dynamics


Task: Identify the team dynamic in different scenarios.

- ◆ A team member dominates discussions, ignoring others' ideas. (Good/Bad?)
- ◆ A project team splits tasks evenly and meets regularly. (Good/Bad?)
- ◆ One member is left out of decision-making. (Good/Bad?)
- ◆ The team brainstorms together and respects all contributions. (Good/Bad?)

Project Team Dynamics



If a team was a musical instrument it would be a xylophone. Each bar is a different size, a different color and makes a different sound when played alone. But when played together, all of the sounds combine to make beautiful music. And so it goes with a project team.



Module 2

1. How to get a project started
 2. selecting project strategically
 3. Project selection models (Numeric /Scoring Models and Non-numeric models)
 4. Project portfolio process
 5. Project sponsor and creating charter
 6. Effective project team
 7. Stages of team development & growth (forming, storming, norming & performing)
 8. Team dynamics.
- 
